



A report on revival and reconstruction of toilets

(Output-1.1a, 1.2a, 3.1a)

September 2015

UN HABITAT
FOR A BETTER URBAN FUTURE

Submitted to
UN-HABITAT
Pulchowk, Lalitpur



Submitted by
CDEC
Chautara, Sindupalchok
Email: cdecf_np@ntc.net.nt

Table of Contents

List of Abbreviation	3
Background	4
Rationale:	4
Objectives:	5
General Objectives:.....	5
Specific Objectives:	5
Project Locations:.....	5
Methodology:.....	5
Human Resources:	6
Output:.....	6
Output 1.1 (a) Revival/Reconstruction of 300 toilets of highly vulnerable families.....	6
Output 1.2 (a) Distribution and proper use of hygiene kit	8
Output 3.1(a) Monitoring and follow up	8
Challenges	9
Conclusion and Recommendations:	9
Annexes.....	9
Annex-1 Minute of V-WASH-CC meeting.....	9
Annex-2: Proposed work plan.....	14
Annex-3: List of Households	15
Annex-4: Minute of joint monitoring by CDECF and UN-HABITAT	27
Annex-5 Photo clips	Error! Bookmark not defined.

List of Abbreviation

CDEC	Community Development and Environment conservation forum
CERF	Central Emergency Relief Fund
D-WASH-CC	District Water Sanitation and Hygiene coordination Committee
DWSS	Department of Water supply and Sewerage
HH	Household
UN	United Nation
UNICEF	United Nations Children's Fund
V-WASH-CC	Village Water Sanitation and Hygiene coordination Committee
VDC	Village Development Committee
WASH	Water Sanitation and Hygiene
WCF	Ward Citizen Forum

Background

After the devastating earthquake of 7.8 magnitudes hit Nepal on 25 April 2015, with strong aftershocks, including a 6.7 magnitude quake on 12th May, people of Sindhupalchowk were badly affected. The quake has resulted in the loss of over 8,700 lives, damaged over half a million houses and 2.8 million people need humanitarian assistance. As UN-Habitat has been working in Sindhupalchowk districts for many years, UN-Habitat has been assisting the Department of Water Supply and Sewerage (DWSS) of Government of Nepal, which serves as the lead of the WASH Cluster and UNICEF (co-lead of the WASH Cluster) in coordinating WASH related interventions in Sindhupalchowk districts.

Considering UN-Habitat's experience in working in these districts and its continued intervention in WASH in these affected districts, UN-Habitat partnered to work with UNICEF and other partners in implementing this project to provide life supporting WASH support to affected communities in Sindhupalchowk through CERF funding. This will complement UN-Habitat's existing regular programme of Sanitation Campaign and emergency programme providing temporary shelters for affected communities in these areas. As UNICEF and UN-Habitat has worked closely together in the WASH sector in Nepal for many years and has also joined hands to execute CERF fund projects in Nepal in 2012 and 2013, this is a strategic partnership at the time of this major disaster to address the WASH need of affected families and restore the previous sanitation and hygiene status of the district.

Rationale:

Before mega earthquake, the sanitation coverage in the district was 33.8% (NMIP, 2011) which has increased to 93% (NMIP 2014). Among GSF districts the worst affected districts by earthquake are Sindhupalchowk, Dolakha and Bhaktapur as well as Rasuwa and Nuwakot where GSF is about to intervene among 17 districts. As per OCHA, out of 336,829 populations, 90% are most affected population (303,146) where 154,604 are women and 139,447 children. The households who have toilets initially have been damaged partially and completely. Therefore, the project has focused on revival/reconstruction of toilets considering the vulnerable population which will provide the opportunity for integrated intervention in the district to reach towards ODF status. Thus, this intervention is to support the government for achieving the national target of total sanitation coverage by 2017.

Earthquake affected population of 5 affected districts

SN	Disaster level	District	Total Popu OCHA	% affected population	Affected Population	HH 5.5 / family	Women	Children
1	1	Bhaktapur	417,659	50	208,829	37,969	106,503	96,061
2	1	Dolakha	213,802	80	171,041	31,098	87,231	78,679
3	1	Sindhupalchowk	336,829	90	303,146	55,117	154,604	139,447
4	1	Nuwakot	325,567	80	260,454	47,355	132,831	119,809
5	1	Rasuwa	54,144	60	32,486	5,907	16,568	14,944
TOTAL			1,348,000		3,320,039	603,643	1,693,220	1,527,218

Objectives:

General Objectives:

To provide support of WASH facilities to earthquake affected communities in Sindhupalchowk district.

Specific Objectives:

To Revive/ reconstruct the toilet of highly vulnerable families

To distribute and ensure the proper use hygiene kit among highly vulnerable families.

Project Locations:

The project is focused in two VDCs of Sindhupalchowk district, namely Sipapokhare , Bhotsipa. Both VDCs are located on the southern part of middle Sindhupalchowk district. The nearest marketing centre is Sipaghat which is accessed by black-topped road (Kathmandu- Helambu Track).The project is running on all wards of the both VDCs.



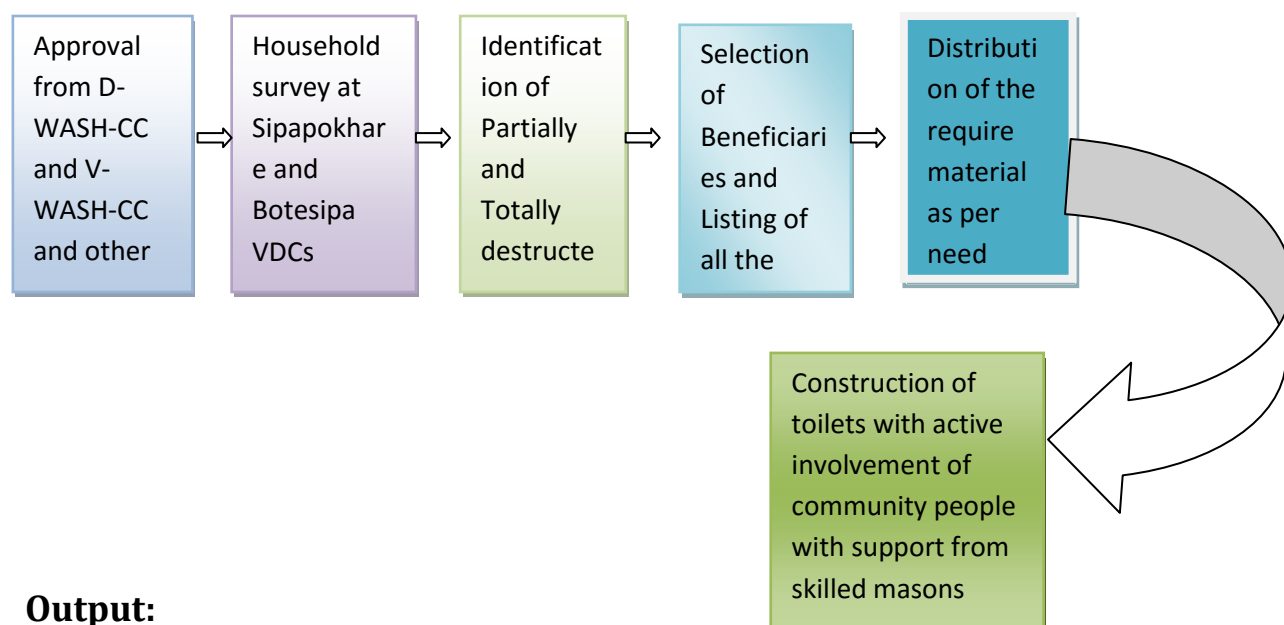
Figure 1: Location map of working VDCs

Methodology:

At first the project detail was discussed in the meeting at VDCs level with VDC secretary, Ward Citizen forum (WCF) and various political parties as well as community people. The project was intervened in the selected two VDCs as Sipapokhare and Botesipa of the Sindhupalchowk district. Initially, the survey was conducted by the Social mobilizers to identify the needs of the community people. After completion of the survey, the detail of the survey with future plan was endorsed by the V-WASH-CC meeting at the VDCs level (Annex-1). Need was classified according to full destruction and partial destruction of the toilets. After For the full destruction the material supported was pan, Pipe, CGI, Cement, Silpolyn and for partial destruction the material provided was pan, silpolyn, CGI, pipe, socket as per need. After the

distribution of the material as per need, with the active participation of the community people with support from the skilled masons the toilet was built.

Process:



Output:

Output 1.1 (a) Revival/Reconstruction of 300 toilets of highly vulnerable families

- A. **Agreement** with CDECF and UN-HABITAT for CERF program on dated 26 August 2015.
- B. **Staff recruitment and mobilization:** The following staffs were recruited and mobilized from 25 August for the successful conduction of CERF program.

S.N	Name	Position	Mobilization date
1	Ram Satyal	Team Leader	1 st September 2015
2	Bijendra Banjade	Program Coordinator	25 th August 2015
3	Rekha Giri	Program Coordinator	1 st September
4	Pushpak Bista	Admin and Finance officer	25 th August 2015
5	Prem Shrestha	Social Mobilizer	25 th August 2015
6	Suntali Tamang	Social Mobilizer	25 th August 2015
7	Sachaman Tamang	Social Mobilizer	25 th August 2015
8	Sitaram Guragain	Social Mobilizer	25 th August 2015
9	Sabina Timalisina	Social Mobilizer	25 th August 2015

- C. **Orientation and Sharing:** After the agreement the Staffs were recruited by CDECF and single day orientation was provided to the staffs and social mobilizers. The team from UN-HABITAT orients and shared about program and operational strategies.
- D. **House hold survey:** The assessment of the two VDCs was done by the social mobilizers. Assessment of the two VDCs revealed the devastating condition of the WASH status.

- E. **Consultation and coordination:** Visit in the VDCs to verify data, sharing and consultation with V/M-WASH-CC on CERF for information dissemination, strategies and working modalities. The regular consultation and meeting with V-WASH-CC and local stakeholders was conducted to verify data, plan and discuss the working modalities and finalization of the working households.
- F. **Market survey and procurement:** The market survey and quotation collection was started immediately after the agreement. After finalization of the HHs, the quotation was reviewed and best supplier was identified for the procurement of the necessary materials.
- G. **Material transportation, storage and distribution:** After the procurement of the material, it was transported to the site and storage was done in separate sites of the selected two VDCs. The material was distributed to the needy people as per the listing which was approved by the V-WASH-CC. Out of total 763, 75% material was distributed at household level.
- H. **Selection and mobilization of masons and volunteers:** The volunteers and masons were selected in each VDC. The 4 masons were selected from both VDCs, who work for the construction of the toilets in the household where the need is identified by the Ward Citizen forum (WCF). The 4 selected Volunteers work for support of the CERF program.
- I. **Construction of the Toilets:** We segregate the Toilet status in the two categories i.e. Partial destructed toilet and completely destructed toilet among the vulnerable groups. The selected masons were mobilized for the construction of the toilet. The revival and reconstruction of toilet data and the progress by the CERF program up to 25 September 2015 are shown below:

Table 1: Status of the Sipapokhare and Botesipa VDC of Sindhupalchowk District

VDC	Total HHs	Status of toilets (toilets in number)				Toilets being constructed by other agencies					Toilets to construct/ revive by CERF Program			Completed		Total
		In good condition	Complete damaged	Partial damage	Total to revive/construct	UNICEF	WVI	UN-Habitat, Shelter	Redcross	Total	Entire damaged	Partial damaged	Total	Completed Entire damage d	Completed partially damage	
Bhotsipa	1221	369	325	177	502	249	0	101	0	350	325	177	502	116	90	206
Sipapokhari	1163	426	167	94	261	242	84	150	0	476	167	94	261	109	80	189
Totl	2384	795	492	271	763	491	84	251	0	826	492	271	763	225	170	395

The total toilet constructed/ revived is listed in annex -2 After the assessment it was identified that the toilet need to be Constructed/Revived in the two VDCs comes to be 763. These numbers may vary slightly till the end of the project.

The HHs listing was made and the materials for the construction of the toilet are distributed as per need to the listed households after the assessment.

J. **Reporting:**

As per our plan regular reporting to the UN-HABITAT twice a week is being done.

K. Case Study:

Chinmaya shrestha is now happy to use toilet

A widow of aged 72, inhabitant of pasaldana-3, Botesipa VDC, Chinmaya builds her toilet with her effort and active participation. She has lost her husband just before earthquake. Her sorrow was not healed completely but nature gave her another shock of devastating earthquake in April 25, 2015. Her house was completely damaged as well as toilet. After the support of the UN-HABITAT/CERF and CDECF she was successful to complete the toilet construction.

She stated with her shy face that “Now, I don’t have to bother about walking a long and finding the place for toilet in jungle/bushes, I was too scared to go to toilet at late night but now I have toilet nearby my house”. She said I am thankful for you all for providing the support for construction of toilet. She has contributed approx Rs.1200 for the construction of toilet. She used such cost for sand and gravels.



She smiled and said “I am very poor, with my own effort I won’t succeed to build toilet, I have to move long for toilet each day, but now I don’t have to worry about it now.”

Output 1.2 (a) Distribution and proper use of hygiene kit

Hygiene kits play an important role promotion of health of the community people. As per the part of the CERF program, we will be distributing the hygiene kit and bucket. The hygiene kit has been procured and will be transported to the site by 27th September, 2015. The hygiene kit will be distributed to all the families whose toilet has be reconstructed/ revealed by the CERF program. The hygiene kit will be given as an award for successful completion of the toilet construction for the households in both VDCs.

Output 3.1(a) Monitoring and follow up

The monitoring and follow up plays an important role in the successful completion of the program. In this program the monitoring and follow up takes place as:

- A. **Monitoring by CDECF:** The board member of the CDECF regularly monitored the overall activities of the CERF program. The regular monitoring by the Team leader, Program coordinators as well as the field staff to achieve the target of the program.

- B. **Joint Monitoring by CDECF and UN-HABITAT team:** Monitoring by the CDECF and UN-HABITAT team was done on 24th September 2015. The minute of the monitoring is attached in annex-
- C. **Monitoring by V-WASH-CC:** The V-WASH-CC monitoring is being planned for the 29th September 2015.
- D. **Monitoring By D-WASH-CC:** The D-WASH-CC monitoring will be done at end of the program. This monitoring will ensure the VDC in the Status of ODF.

Challenges

- Most of the people are in the trauma of earthquake till date.
- Difficult geographical territory for the transportation of logistics.
- Strike by the different political parties at terai made scarcity of the material at supplier level, which hinder the immediate progress.
- People are internally displaced and people are making settlement slowly which hinder the accurate data collection, hence data is fluctuating.
- Displaced people are seeking their own place (from where they are displaced) for construction of new houses, so people trying to build toilet in the place where they are planning to build house in near future.
- The short duration of program is being challenge for completion of all the program task

Conclusion and Recommendations:

Although the duration of program was very short, the CERF program was successful for the completion of 395 (52%) toilets up to 25th September, 2015 with continuous monitoring by the CDECF team and UN-HABITAT team. The program was completed in time as per plan by our side but sanitation kits are not delivered in site till date. Due to Teej festival and day of constitution announcement, it was disturbed in work. And also materials are not available in the market due to strike of Terai. 100% target will be achieved up to 15th October, 2015.

Annexes

Annex-1 Minute of V-WASH-CC meeting

- (ક) કામરૂપનો વારાગ્ર આગળી પુલ્લવંધા
- (બ) કામરૂપનો દાનવદ્ય કાલો પ્રાપ્તિ પુલ્લવંધા
- (ગ) કામરૂપનો અદનાતિ ગાલિવંધો પુલ્લવંધા
- (દ) કાકુલાપત તાર પુલ્લવંધા
- (૬) વ્યાપાગી મહાવળ પુલ્લવંધા
- (૭) ગ્રામલ દનદયીના ચીપી તિમાલ પુલ્લવંધા
- (૮)

एखादा तू निर्माण तू मशीन कुणकुण ठाई UN-Habitat /
CIED सहयोगा Citect सारित्रकरणा कुणकुण ठाई
कालिदास हारकुण ठाई सारित्रकरणा पड्डे कायदा अथ सिंग
पेवरे जावरे ठाई सारित्र लाई आनकामी कायदा ठाई निर्माण
सर्वकार नमन ठाई

પ્રજ્ઞાવાદ ન ઇ નિર્ણય ન એ મળી દેવદાસ ગાંધી UN-Habitat
2014 સ્વાસ્થ્યગ્રામ સ્કેપ ઓ સ્વચ્છિતરંગા માત્ર દિવાળીપર
છાડવિનાશ સમિતિના પત્રકો દરમિયાન પુરી થયાથ
વિવેક રિપોર્ટ ગાંધીજી ૨ ગાંધીજીના મુખે જાતજાતી
ગતિઓ કરા સ્વચ્છતા સ્થાપા નિર્ણય ગતિઓ ।

प्रस्ताव नं ३ निमेष नं २। माफी हलचल गर्दा ON-Habibin
उ CREF ठो आधिक तथा प्राविधिक सम्पत्तिको cdefct
सहजिब्ररमा यस पिपपोस्वेरा कार्य सुक्त सम्पत्ति
पहुच कायस्थ सुचाक गर्न भए गाडविताश समिति
वास सहजति जालिम्न कुरा सर्वपन्त रूपमा पारि
गर्दिनो ।

पुरखाने के लिए निर्धारित ८.६४ माह की कलाकृत गार्ड अप
विधारणोन्मुख गाडोवेडावा समितिमा गाडो खारेज खाता
खोलोपानो व्यवस्था तथा स्वच्छता व्यवस्था समिति
वडा समितिमा छ, जिल्ला समन्वयी त अलगम १
२ जिल्ला खादिख खोलोपानो तथा व्यवस्था तथा
स्वच्छता व्यवस्था समिति, जिल्ला खोलोपानो

UN- Habitat, code of law अदुगमन गन मिमवला
पहाडने निजीय अरु पुरान अरु पानि गारियो ।

प्रस्ताव नं ६: निर्णय नं ६ माघी हलकल जहां घण सिपायोंको
जोड विकास स्थितिना व्यवस्था ६ पहुँच कायकन वात सामान
हुवानी जहां १८६ को केससली ~~सुप्रीमको~~ ^{सुप्रीमको} प्रधानता देवारी
के महिला विकासता १/६ के ~~सुप्रीमको~~ ^{सुप्रीमको} २/३/६ के
माथिको न्यायन आगिने कानेता सामान जाओपम जने
निर्णय गतिको ।

પરિણામ તો જી. નિર્મય તો આગળી ફલજલ ગળી થયું
મિયાપોચેરે ગાડાવિદ્યાશ સુખિતિના સમાલ ચરચુરી
દુગોટ વડા નાગેલું કચ્છ કાઢત ગાડવિદ્યાશ સુખિતિના
નામાવળિ પેશા ગર્ન ગાડ વિદ્યાશ સુખિતિના દુગોટ ભાડ
સરસકાંડ પહુંચ કામકાંઠ કાઢત વચગોળ સ્પલવદ
ગારાગે નિર્મય ગરિયો ।

प्रस्ताव नं 6 काशी इलकुल गरी ग्राम विभागीय क्षेत्र
पुरी मिति. १९९९ आर्थिक मिति १९९९ ON 1. 1994 वा
महोदय १९९९ ज. का. वि. सं. स. स. स. वि. वि. वि. वि.
वा. वा. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि.
वा. वा. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि.
वा. वा. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि. वि.

[illegible]

V-WASH-CC meeting at Sipapokhari for endorsement of CERF program, Beneficiaries selection and logistic storage

प्रस्ताव नं. १ निर्माण कठ माध्यम एल्लुल गरी UN/PROBITH
आर्थिक तथा प्राविष्टि व्यवस्था आमुदायिक विकास तथा
वर्ग व्यवस्था प्रत्येक व्यवस्थाकर्ता विद्यापीठ गरी जाउवि
आगत विस्तार कानि ५ त्ता ३० छरदुगीता सैव
व्यापारी वित्तन गरी सैव कही छरदुगीता UN/PROBITH
अस्थापी छरदुगी परेको सैव कानि गतमा कही जाय
कानि आकषमता परे छरदुगीता व्यापार व्यवस्था
नै आगत विस्तार कानि ।

[illegible]

V-WASH-CC meeting at Sipapokhari for endorsement of CERF program, Beneficiaries selection and logistic storage

आज मिति २०७२ साल भाद्र शुक्ल गतेका दिन यस भोट सिपा गा.वि.स. मा UN-HABITAT/CERF र COECF को सह योगमा सन्चालित भूकम्प क्षिति कारकमा घरसफाई कार्यक्रमका नामो यो यो गीति शर्मा V-WASH-CC का संयोजक श्री पुर्ण प्रसाद कुशोल को संयोजकत्वमा तपसिलको उपस्थितिमा बैठक विभिन्न प्रश्नमा उपर इलकल गरियो।			
तपसिल उपस्थिति			
१. संयोजक श्री :-	पुर्ण प्रसाद कुशोल		
२. सहसंयोजक :-	दीर्घा कुशोल		
३. ने.कु.प्र.मात्रे :-	बाबुराम लामा		
४. श्री ने.कु.प्र.मात्रेको :-	एक व. गोपा		
५. नेपाली भाषाको :-	पुष्प प्रसाद भट्टराई		
६. राष्ट्रपति :-	आमर व. भट्टराई	अमर	
७. सहसंयोजक :-	राधिका भट्टराई (का.नं. १)		
८. " :-	ने.प्र.स.द. भानुवार्ध (का.नं. २)	अ.प्र.स.द.	
९. " :-	आमर व. प्रसाद (संयोजक का.नं. ३)		
१०. " :-	न.प्र.स.द. भट्टराई (का.नं. ४)		
११. " :-	यु.प्र.स.द. भट्टराई (का.नं. ५)	म.प्र.स.द.	
१२. " :-	निलमा व. कुशोल	ला.प्र.स.द.	
१३. " :-	रमेश भट्टराई (का.नं. ६)		
१४. " :-	वीर व. लामा (संयोजक का.नं. ७)		
१५. " :-	पुष्प प्रसाद (संयोजक का.नं. ८)		
१६. " :-	हरि प्रसाद कुशोल (का.नं. ९)		
१७. " :-	रविश भट्टराई (हुडी रेश कुशोल, सुकेश)		
१८. " :-	श्रीमा लामा		
१९. " :-	सजिमा श्रेष्ठ (का.नं. १०)		
२०. " :-	विनोद भट्टराई (का.नं. ११)		
२१. " :-	राजन भट्टराई (का.नं. १२)		
२२. " :-	राजेश लाल श्रेष्ठ (का.नं. १३)		
२३. " :-	हनि प्रसाद नेपाल (संयोजक का.नं. १४)		
२४. " :-	राज प्रसाद शर्मा (का.नं. १५)		
२५. " :-	श. रेश्मा राण भट्टराई		
२६. " :-	हिमालेन नेपाल (का.नं. १६)		
२७. " :-	निलक प्रसाद कुशोल (मानव संसाधन)	अ.प्र.स.द.	
२८. " :-	आमर भट्टराई (का.नं. १७)	अमर	
२९. " :-	राजाराण भट्टराई (का.नं. १८)		
३०. " :-	रमेश प्रसाद भट्टराई (का.नं. १९)		
३१. " :-	पुष्प प्रसाद नेपाल (का.नं. २०)		
३२. " :-	लो. व. पराशुराम (का.नं. २१)		
३३. " :-	के. व. शर्मा (का.नं. २२)		
३४. " :-	मान प्रसाद लामा (का.नं. २३)	मान	
३५. " :-	सुरेश्वरी कुशोल (का.नं. २४)	सुरेश्वरी	
३६. " :-	प्रमिला लामा (का.नं. २५)	प्रमिला	
३७. " :-	रामचन्द्र शर्मिष्ठा (का.नं. २६)		
३८. " :-	एकता लामा	एकता	
३९. " :-	प्रमिला लामा		
४०. " :-	विष्णु प्रसाद लामा		
४१. " :-	तुलसी प्रसाद लामा		
४२. " :-	विष्णु प्रसाद लामा		
४३. " :-	रिष्ठा प्रसाद लामा		
४४. " :-	कृष्ण प्रसाद लामा		
४५. " :-	भक्त व. कुशोल		
४६. " :-	शोभा व. लामा		
४७. " :-	विजय कुशोल	COECF/PC	
४८. " :-	पवन भट्टराई	COECF/PC	
४९. " :-	सिरिता शर्मा	COECF/PC	
५०. " :-	विष्णु शर्मा भट्टराई		
५१. " :-	यु.प्र.स.द. भट्टराई		
५२. " :-	पुष्प प्रसाद		
५३. " :-	जे. आर. शर्मा		
५४. " :-	सन्तमान लामा	COECF	

V-WASH-CC meeting at Bhotesipa VDC for endorsement of CERF program, Beneficiaries selection and logistic storage

[illegible]

Annex-3: List of Households

SN	Name	Materials needed	Type of damage	Status
1	Hom Nath Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
2	bishnu Sarki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
3	Gokul Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
4	Ramesh Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
5	Ram Bdr Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
6	Prem Prd Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
7	Ambica Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
8	Susma Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
9	khadanantha Dungol	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
10	JhamkaNatha dangol	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

11	Bhadra kanta Dangol	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
12	Ramkrishna Bogati	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
13	Dhan Maya Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
14	Ram Chandra Dhakal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
15	Dalachandra Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
16	Jagatnath Adhikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
17	Sano Napit	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
18	Ananda Raj Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
19	Bishnu Prd dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
20	Jaya Prd Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
21	Utshav Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
22	Sabitri Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
23	Bhabi Lal Kami	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
24	MuktiNath Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
25	Madan Krishna Adikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
26	Lal Chandra Adhikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
27	JayRam Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
28	Danda Kumari Adikri	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
29	Hom Prd Gajarat	CGI,Spln	Partial	Completed
30	Dadi lal Adhakari	CGI,Spln	Partial	Completed
31	Chetnath Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
32	Binda Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
33	Sobha Acharaya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
34	Chandra Bdr Neupane	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
35	Nir kumari Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
36	Subdra Neupane	Spln	Partial	Completed
37	Sanu Maya Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
38	Gokul Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
39	Sun Bdr Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
40	kalu Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

41	Chandra Ku Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
42	Baliman Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
43	Jit Bdr Tamang	CGI,Spln	Partial	Completed
44	Netra Bdr Tamang	CGI,Spln	Partial	Completed
45	Ambar Bdr Tamang	CGI,Spln	Partial	Completed
46	Shir Bdr Tamang	CGI,Spln	Partial	Completed
47	Bhim Bdr Tamang	CGI,Spln	Partial	Completed
48	Sukurani Tamang	CGI,Spln	Partial	Completed
49	Santosh Dhungana	CGI,Spln	Partial	Completed
50	Man kajiTamang	CGI,Spln	Partial	Completed
51	Pratap Sing Tamang	CGI,Spln	Partial	Completed
52	Hem Bdr tamang	CGI,Spln	Partial	Completed
53	Kancha Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
54	Jamuna Damini	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
55	Prem Prd Pokheral	CGI,Spln	Partial	Completed
56	Raj kumar Dangal	CGI,Spln	Partial	Completed
57	Lok Bdr Sarki	CGI,Spln	Partial	Completed
58	Akal Sarki	CGI,Spln	Partial	Completed
59	Krishna Prd Bhattarai	CGI,Spln	Partial	Completed
60	Bashudev Bhattarai	CGI,Spln	Partial	Completed
61	Echharam Dangal	CGI,Spln	Partial	Completed
62	Krishna Kumari Neupane	CGI,Spln	Partial	Completed
63	Sudha Neupane	Cgl,Spln	Partial	Completed
64	Ram Kumar Neupane	pan	Partial	Completed
65	Man Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
66	Rudra Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
67	Naresh Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
68	Tara Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
69	Krishna Gopal Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
70	Mahedra Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

71	Ramesh Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
72	Balkrishna Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
73	Am Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
74	Bom Bdr Shrestha	CGI,Spln	Partial	Completed
75	Babulal Shrestha	CGI,Spln	Partial	Completed
76	Arjun Shresth	CGI,Spln	Partial	Completed
77	Dhurba Shrestha	CGI,Spln	Partial	Completed
78	Susma Karki	CGI,Spln	Partial	Completed
79	Nabaraj Shrestha(1)	CGI,Spln	Partial	Completed
80	Nabaraj Shrestha(2)	CGI,Spln	Partial	Completed
81	Keshav Shrestha	CGI,Spln	Partial	Completed
82	Dal Bdr Shrestha(Thulo)	CGI,Spln	Partial	Completed
83	Subba Shrestha	CGI,Spln	Partial	Completed
84	Man Bdr Shrestha(sano)	CGI,Spln	Partial	Completed
85	Nil Bdr Shrestha	CGI,Spln	Partial	Completed
86	Hira Devi Shrestha	CGI,Spln	Partial	Completed
87	Man Bdr Shrestha(2)	CGI,Spln	Partial	Completed
88	Hira Lal Shrestha	CGI,Spln	Partial	Completed
89	Dilip Shrestha	CGI,Spln	Partial	Completed
90	Khadka Bdr Shrestha	CGI,Spln	Partial	Completed
91	kamal Shrestha(A)	CGI,Spln	Partial	Completed
92	Tara Bdr Shrestha	Pan,Spln,CGI	Partial	Completed
93	Hell Bdr Shrestha	CGI,Spln	Partial	Completed
94	Sundar Prd Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
95	Prem Prd Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
96	kalpane Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
97	Asha bashnet	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
98	Chaal Kumari ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
99	Dhurba Bdr Magar	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
100	Nabaraj Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

101	Jamuna Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
102	Lila Bdr Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
103	Nakul Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
104	Manika Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
105	Kedar Prasad Bhattarai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
106	Chitra Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
107	Rajendra Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
108	krishna Bdr Bhujel	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
109	Dev Raj Giri	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
110	Gaan Bdr Bashnet	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
111	Juna Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
112	Ramhari Karki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
113	Deep Bdr Pandey	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
114	Chandrawati Karki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
115	Nil Bdr. Budathoki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
116	Ramesh Nepali	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
117	Check Bdr Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
118	Sunita Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
119	Sitaram Thapa	Cement,Spln,Pipe,CGI	Partial	Completed
120	Durga Bdr Ghimire	CGI,Spln	Partial	Completed
121	Purna Pd Dangal	CGI,Spln	Partial	Completed
122	Indra Bdr Karki	CGI,Spln	Partial	Completed
123	Makhmali Dhungana	CGI,Spln	Partial	Completed
124	Taranath Chulagai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
125	Suman Dotel	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
126	Devi Prd Dotel	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
127	Surya Prd Chulagai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
128	Ramesh Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
129	Sudarshan Tewari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
130	Naryan Bdr Parajuli	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

131	Ram Bdr Baneya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
132	Dal Bdr Shrestha	CGI,Spln	Partial	Completed
133	Padam Bdr Shrestha	CGI,Spln	Partial	Completed
134	Narendra Chulagai	CGI,Spln	Partial	Completed
135	Khurnath Chulagai	CGI,Spln	Partial	Completed
136	Khoj Prd Dotel	CGI,Spln	Partial	Completed
137	YamNath Chulagai	pan	Partial	Completed
138	Udhaya Baneya	CGI,Spln	Partial	Completed
139	Hasta Kumari Baneya	Pan,pipe	Partial	Completed
140	Krishna Pd Acharaya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
141	Nabaraj Acharaya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
142	Shyam Bdr shrestha	CGI,Spln	Partial	Completed
143	Susma Kumari shrestha	CGI,Spln	Partial	Completed
144	Man Bdr Shrestha	CGI,Spln	Partial	Completed
145	Ganga Ram Shrestha	CGI,Spln	Partial	Completed
146	Dipesh Shrestha	CGI,Spln	Partial	Completed
147	Shiba Prd Adhikari	CGI,Spln	Partial	Completed
148	Harihar Adhikari	CGI,Spln	Partial	Completed
149	Dhurba Prd Sigdel	CGI,Spln	Partial	Completed
150	Keshav chaulagain	CGI,Spln	Partial	Completed
151	pursottam Tiwari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
152	Kendra Bdr. Tamang	CGI,Spln	Partial	Completed
153	Bil Bdr. Tamang	CGI,Spln	Partial	Completed
154	Ram Bdr. Tamang	CGI,Spln	Partial	Completed
155	jayantinath Adhikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
156	Ram Bdr Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
157	Hari kumar Neupane	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
158	Dil Bdr. Bokati	Cgl,Spln	Partial	Completed
159	Kami Sarki	Cgl,Spln	Partial	Completed
160	Balkrisna Neupane	Cgl,Spln	Partial	Completed

161	Tom Bdr. Bhattarai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
162	Kami Sarki	CGI,Spln	Partial	Completed
163	Goma BK	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
164	Madan krishna adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
165	Top pd. Bhattarai	CGI,Spln	partial	Completed
166	Juna Nepali	Cement,Spln,Pan,Pipe,CGI	complete	Completed
167	Hom Nath Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
168	bishnu Sarki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
169	Gokul Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
170	Ramesh Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
171	Ram Bdr Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
172	Prem Prd Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
173	Ambica Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
174	Susma Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
175	khadanantha Dungol	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
176	JhamkaNatha dangol	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
177	Bhadra kanta Dangol	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
178	Ramkrishna Bogati	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
179	Dhan Maya Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
180	Ram Chandra Dhakal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
181	Dalachandra Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
182	Jagatnath Adhikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
183	Sano Napit	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
184	Ananda Raj Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
185	Bishnu Prd dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
186	Jaya Prd Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
187	Utshav Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
188	Sabitri Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
189	Bhabi Lal Kami	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
190	MuktiNath Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

191	Madan Krishna Adikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
192	Lal Chandra Adhikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
193	JayRam Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
194	Danda Kumari Adikri	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
195	Hom Prd Gajarat	CGI,Spln	Partial	Completed
196	Dadi lal Adhakari	CGI,Spln	Partial	Completed
197	Chetnath Adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
198	Binda Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
199	Sobha Acharaya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
200	Chandra Bdr Neupane	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
201	Nir kumari Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
202	Subdra Neupane	Spln	Partial	Completed
203	Sanu Maya Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
204	Gokul Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
205	Sun Bdr Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
206	kalu Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
207	Chandra Ku Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
208	Baliman Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
209	Jit Bdr Tamang	CGI,Spln	Partial	Completed
210	Netra Bdr Tamang	CGI,Spln	Partial	Completed
211	Ambar Bdr Tamang	CGI,Spln	Partial	Completed
212	Shir Bdr Tamang	CGI,Spln	Partial	Completed
213	Bhim Bdr Tamang	CGI,Spln	Partial	Completed
214	Sukurani Tamang	CGI,Spln	Partial	Completed
215	Santosh Dhungana	CGI,Spln	Partial	Completed
216	Man kajiTamang	CGI,Spln	Partial	Completed
217	Pratap Sing Tamang	CGI,Spln	Partial	Completed
218	Hem Bdr tamang	CGI,Spln	Partial	Completed
219	Kancha Tamang	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
220	Jamuna Damini	Cement,Spln,Pan,Pipe,CGI	Complete	Completed

221	Prem Prd Pokheral	CGI,Spln	Partial	Completed
222	Raj kumar Dangal	CGI,Spln	Partial	Completed
223	Lok Bdr Sarki	CGI,Spln	Partial	Completed
224	Akal Sarki	CGI,Spln	Partial	Completed
225	Krishna Prd Bhattarai	CGI,Spln	Partial	Completed
226	Bashudev Bhattarai	CGI,Spln	Partial	Completed
227	Echharam Dangal	CGI,Spln	Partial	Completed
228	Krishna Kumari Neupane	CGI,Spln	Partial	Completed
229	Sudha Neupane	Cgl,Spln	Partial	Completed
230	Ram Kumar Neupane	pan	Partial	Completed
231	Man Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
232	Rudra Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
233	Naresh Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
234	Tara Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
235	Krishna Gopal Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
236	Mahedra Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
237	Ramesh Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
238	Balkrishna Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
239	Am Bdr Shrestha	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
240	Bom Bdr Shrestha	CGI,Spln	Partial	Completed
241	Babulal Shrestha	CGI,Spln	Partial	Completed
242	Arjun Shresth	CGI,Spln	Partial	Completed
243	Dhurba Shrestha	CGI,Spln	Partial	Completed
244	Susma Karki	CGI,Spln	Partial	Completed
245	Nabaraj Shrestha(1)	CGI,Spln	Partial	Completed
246	Nabaraj Shrestha(2)	CGI,Spln	Partial	Completed
247	Keshav Shrestha	CGI,Spln	Partial	Completed
248	Dal Bdr Shrestha(Thulo)	CGI,Spln	Partial	Completed
249	Subba Shrestha	CGI,Spln	Partial	Completed
250	Man Bdr Shrestha(sano)	CGI,Spln	Partial	Completed

251	Nil Bdr Shrestha	CGI,Spln	Partial	Completed
252	Hira Devi Shrestha	CGI,Spln	Partial	Completed
253	Man Bdr Shrestha(2)	CGI,Spln	Partial	Completed
254	Hira Lal Shrestha	CGI,Spln	Partial	Completed
255	Dilip Shrestha	CGI,Spln	Partial	Completed
256	Khadka Bdr Shrestha	CGI,Spln	Partial	Completed
257	kamal Shrestha(A)	CGI,Spln	Partial	Completed
258	Tara Bdr Shrestha	Pan,Spln,CGI	Partial	Completed
259	Hell Bdr Shrestha	CGI,Spln	Partial	Completed
260	Sundar Prd Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
261	Prem Prd Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
262	kalpane Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
263	Asha bashnet	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
264	Chaal Kumari ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
265	Dhurba Bdr Magar	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
266	Nabaraj Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
267	Jamuna Dangal	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
268	Lila Bdr Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
269	Nakul Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
270	Manika Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
271	Kedar Prasad Bhattarai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
272	Chitra Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
273	Rajendra Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
274	krishna Bdr Bhujel	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
275	Dev Raj Giri	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
276	Gaan Bdr Bashnet	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
277	Juna Ghimire	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
278	Ramhari Karki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
279	Deep Bdr Pandey	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
280	Chandrawati Karki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed


281	Nil Bdr. Budathoki	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
282	Ramesh Nepali	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
283	Check Bdr Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
284	Sunita Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
285	Sitaram Thapa	Cement,Spln,Pipe,CGI	Partial	Completed
286	Durga Bdr Ghimire	CGI,Spln	Partial	Completed
287	Purna Pd Dangal	CGI,Spln	Partial	Completed
288	Indra Bdr Karki	CGI,Spln	Partial	Completed
289	Makhmali Dhungana	CGI,Spln	Partial	Completed
290	Taranath Chulagai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
291	Suman Dotel	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
292	Devi Prd Dotel	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
293	Surya Prd Chulagai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
294	Ramesh Sapkota	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
295	Sudarshan Tewari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
296	Naryan Bdr Parajuli	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
297	Ram Bdr Baneya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
298	Dal Bdr Shrestha	CGI,Spln	Partial	Completed
299	Padam Bdr Shrestha	CGI,Spln	Partial	Completed
300	Narendra Chulagai	CGI,Spln	Partial	Completed
301	Khurnath Chulagai	CGI,Spln	Partial	Completed
302	Khoj Prd Dotel	CGI,Spln	Partial	Completed
303	YamNath Chulagai	pan	Partial	Completed
304	Udhaya Baneya	CGI,Spln	Partial	Completed
305	Hasta Kumari Baneya	Pan,pipe	Partial	Completed
306	Krishna Pd Acharaya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
307	Nabaraj Acharaya	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
308	Shyam Bdr shrestha	CGI,Spln	Partial	Completed
309	Susma Kumari shrestha	CGI,Spln	Partial	Completed
310	Man Bdr Shrestha	CGI,Spln	Partial	Completed


311	Ganga Ram Shrestha	CGI,Spln	Partial	Completed
312	Dipesh Shrestha	CGI,Spln	Partial	Completed
313	Shiba Prd Adhikari	CGI,Spln	Partial	Completed
314	Harihar Adhikari	CGI,Spln	Partial	Completed
315	Dhurba Prd Sigdel	CGI,Spln	Partial	Completed
316	Keshav chaulagain	CGI,Spln	Partial	Completed
317	pursottam Tiwari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
318	Kendra Bdr. Tamang	CGI,Spln	Partial	Completed
319	Bil Bdr. Tamang	CGI,Spln	Partial	Completed
320	Ram Bdr. Tamang	CGI,Spln	Partial	Completed
321	jayantinath Adhikari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
322	Ram Bdr Dhungana	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
323	Hari kumar Neupane	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
324	Dil Bdr. Bokati	Cgl,Spln	Partial	Completed
325	Kami Sarki	Cgl,Spln	Partial	Completed
326	Balkrisna Neupane	Cgl,Spln	Partial	Completed
327	Tom Bdr. Bhattarai	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
328	Kami Sarki	CGI,Spln	Partial	Completed
329	Goma BK	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
330	Madan krishna adhakari	Cement,Spln,Pan,Pipe,CGI	Complete	Completed
331	Top pd. Bhattarai	CGI,Spln	partial	Completed
332	Juna Nepali	Cement,Spln,Pan,Pipe,CGI	complete	Completed


Annex-4: Minute of joint monitoring by CDECF and UN-HABITAT


भारत प्रति २०६२ साल आश्विन ७ गतेका दिन UN-HABITAT को सहयोग र साथै दाखिल बिकास तथा कामावाला र्ग-समा मन्त्रालयको सहजीकरण। शिवापोखो ३ अन्तरिक्षा जा.ति.श.मा सन्धानित CERF कार्यक्रम अन्तर्गत UN-HABITAT/CDECF को सहयोगबाट त्रिभुवन नगरपालिकाको आवासनयक प्रमुख कार्यक्रम UN-HABITAT, CDECF र स्थानीय वडा समिति प्रमुखको प्रतिनिधि हस्ताक्षर तपसिलको उपाधिनीमा सम्पन्न गरियो।


१. UN-HABITAT मुखिल राज ठोंग्र 


२. UN-HABITAT, DC हुनी राइजे मोल्डा 


३. UN-HABITAT बृहत् युवेदी 


४. मध्यम CDECF आरदा प्रसाद शुम्भेरा 

५. CDECF Team leader राम सुब्बात 

६. CDECF PC विजेंद्र बज्राडे 

७. CDECF नेत्र प्रसाद आचार्य 

८. CDECF PC हरिता डर्जी 

९. CDECF बाबुराम श्रेष्ठ 

१०. कामागलिप्रान्त रेपोरक प्रेरक्षित-३ दिपेंद्र श्रेष्ठ 

११. CDECF प्रेम कुमार श्रेष्ठ 

१२. CDECF सुविना तिमल्सिना 



Full damaged toilet



New constructed latrine



Under construction



Materials transportation



Materials distribution



During Revival of Toilet
